



New Stoneham High School
Project Number: 20033

Site Rep. - Bob Smith

WEEKLY REPORT #15 - Week Ending 2/11/23

Weekly Man Power Summary		Mon.	Tue.	Wed.	Thurs.	Fri.	Sat	Total
Trade:	Subcontractor:	6-Feb	7-Feb	8-Feb	9-Feb	10-Feb	11-Feb	
Owners Project Manager	SMMA	2	1	3	2	2	0	10
General Contractor	Consigli Construction Co.	9	10	10	10	10	0	49
Architect	Perkins & Will	0	0	2	0	0	0	2
Geotech Eng.	LGCI	0	0	0	1	0	0	1
Civil Eng.	Nitsch Engineering	0	0	0	0	0	0	0
Landscape Arch.	Warner Larson	0	0	0	0	0	0	0
Structural Eng.	B+AC	0	0	1	0	0	0	1
M/E/P/FP Eng.Geowell Eng.	McPhail Associates	0	3	0	0	1	0	4
Testing Company	UTS	0	2	0	2	0	0	4
Environmental Consultant	Universal Environmental Consult	0	0	0	0	0	0	0
Site Contractor	Marois Brothers	5	5	5	5	5	0	25
Blasting	Maine Drilling and Blasting	0	0	0	1	0	0	1
Concrete	Riggs	17	20	21	19	20	0	97
Masonry		0	0	0	0	0	0	0
Struc Steel	Norgate Metal	0	0	0	0	0	0	0
Misc Metal		0	0	0	0	0	0	0
Metal Panels		0	0	0	0	0	0	0
Finish Carpentry		0	0	0	0	0	0	0
Waterproofing, Dampproofing & Caulking	Heritage Restoration	0	0	0	0	0	0	0
Spray Foam Insulation		0	0	0	0	0	0	0
Fireproofing		0	0	0	0	0	0	0
Firestopping		0	0	0	0	0	0	0
Roofing		0	0	0	0	0	0	0
Glass & Glazing		0	0	0	0	0	0	0
Doors, Frames & Hardware		0	0	0	0	0	0	0
Overhead Doors		0	0	0	0	0	0	0
Aluminum Entrances & Storefronts		0	0	0	0	0	0	0
Windows		0	0	0	0	0	0	0
Tile		0	0	0	0	0	0	0
Acoustical Tile		0	0	0	0	0	0	0
Resilient Flooring		0	0	0	0	0	0	0
Painting		0	0	0	0	0	0	0
GWB & Framing		0	0	0	0	0	0	0
Wood Flooring		0	0	0	0	0	0	0
Wall Coverings		0	0	0	0	0	0	0
Lab Casework		0	0	0	0	0	0	0
Specialties		0	0	0	0	0	0	0
Auditorium Seating		0	0	0	0	0	0	0
Equipment		0	0	0	0	0	0	0
Bleachers		0	0	0	0	0	0	0
Gym Equipment		0	0	0	0	0	0	0
Furnishings		0	0	0	0	0	0	0
Furnishings		0	0	0	0	0	0	0
Elevators		0	0	0	0	0	0	0
Fire Protection		0	0	0	0	0	0	0

Site Rep. - Bob Smith

WEEKLY REPORT #15 - Week Ending 2/11/23

Plumbing		0	0	0	0	0	0	0	
HVAC		0	0	0	0	0	0	0	
Electrical	Jupiter Electric	0	2	0	2	0	0	4	
Telecom		0	0	0	0	0	0	0	
Security		0	0	0	0	0	0	0	
Earthwork	Chesapeake Geothermal	0	1	2	0	0	0	3	
Landscaping		0	0	0	0	0	0	0	
Playground Equipment		0	0	0	0	0	0	0	
Temp. Fencing	Riggs	0	0	0	0	0	0	0	
Other		0	0	0	0	0	0	0	
Total Weekly Manpower			34	45	42	42	38	0	201

Weekly Progress

Excavated for footings in area "C" and for footings in area "D". Winter protection & temporary heating of foundations, trenches and footing excavations. Set forms, tied rebar for walls, footings, and grade beams in area "B", area "C" walls and footings, and area "A" footings. Pour concrete and strip forms for footings, grade beams and walls in area "B", area "C" walls and footings, and area "A" footings. Excavated, spread a layer of sand, installed conduits, formed, poured concrete around conduits, stripped forms and backfilled Electrical and Tel/Com ductbank on the South side and Northwest side utility corridors. Installation of water main, sprinkler main and hydrant.

Project Schedule Key Dates:	Activity ID	Baseline Start Finish Dates	Actual Start Finish Dates		Comments
Geothermal Wells Start	A7090	8/9/2022	10/10/2022		
Geothermal Wells Complete	A8030	4/18/2023			
Concrete foundations Start	A8020	9/28/2022	10/31/2022		
Concrete Foundations Complete	A9120	2/10/2023			
Structural Steel Start	A8160	3/28/2023			
Structural Steel Complete	A10610	8/24/2023			

Photos

All images need the consent of Consigli Construction prior to being released to the public.



PREPPING PRIMARY ELECTRICAL DUCTBANK



INSTALLING CONDUIT IN PRIMARY DUCTBANK



ENCASING ELECTRICAL DUCTBANK IN CONCRETE



INSTALLING WATER PIPING AND HYDRANT




HEATING & PROTECTING FOOTINGS AREA "B"



POURING GRADE BEAMS & FOOTINGS IN AREA "B"



POURING GRADE BEAMS IN AREA "B"

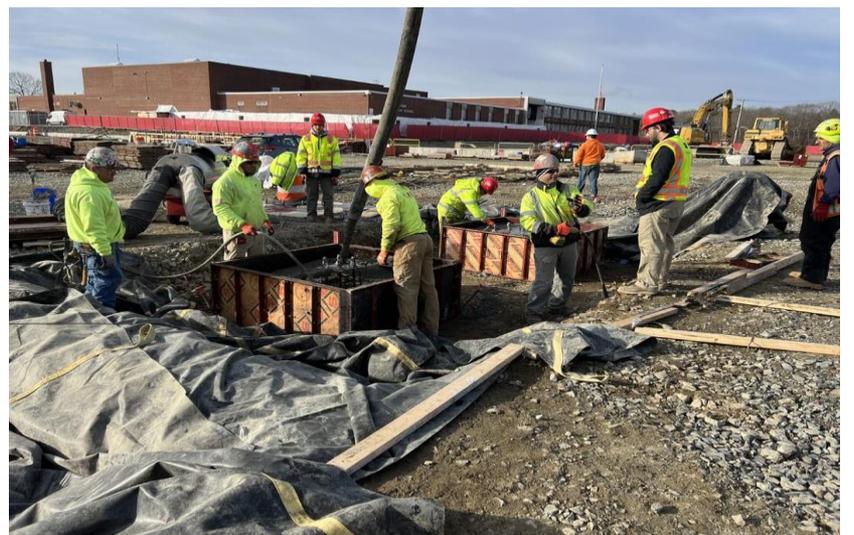

POURING FOOTINGS IN AREA "A"



HEATING WALLS AFTER CONCRETE PLACEMENT



STRIPPING FORMS IN AREA "B"



BUILDING SITE PROGRESS LOOKING SOUTH



DRONE PROGRESS IMAGE
