

Site Rep. - Bob Smith

WEEKLY REPORT #22 - Week Ending 4/01/23

Weekly Man Power Summary		Mon.	Tue.	Wed.	Thurs.	Fri.	Sat	Total
Trade:	Subcontractor:	27-Mar	28-Mar	29-Mar	30-Mar	31-Mar	1-Apr	
Owners Project Manager	SMMA	2	2	2	2	2	0	10
General Contrator	Consigli Construction Co.	11	12	9	10	10	0	52
Architect	Perkins & Will	0	0	3	0	0	0	3
Geotech Eng.	LGCI	0	0	1	1	1	0	3
Civil Eng.	Nitsch Engineering	0	0	0	0	0	0	0
Landscape Arch.	Warner Larson	0	0	0	0	0	0	0
Structural Eng.	B+AC	0	0	0	0	0	0	0
M/E Eng.	BALA Consulting Engineers	0	0	0	0	0	0	0
Testing Company	UTS	1	2	2	1	1	0	7
Enviromental Consultant	Universal Environmental Consultan	0	0	0	0	0	0	0
Site Contractor	Marois Brothers	7	7	10	9	10	0	43
Demolition-Abatement	Costello Dismantling	0	0	0	0	0	0	0
Concrete	Riggs	16	15	15	14	15	0	75
Masonry	Fernandes Masonry	0	0	0	0	0	0	0
Struc Steel	Stellar Erectors-Chelmsford Crane	10	10	13	18	3	0	54
Misc Metal	Avid Iron Works	0	0	0	0	0	0	0
Metal Panels	Riggs	0	0	0	0	0	0	0
Finish Carpentry		0	0	0	0	0	0	0
Waterproofing	Heritage Restoration	1	0	2	0	0	0	3
AVB & Caulking	P.J. Spillane	0	0	0	0	0	0	0
Spray Foam Insulation		0	0	0	0	0	0	0
Fireproofing	H. Carr & Sons	0	0	0	0	0	0	0
Firestopping		0	0	0	0	0	0	0
Roofing	Greenwood Industries	0	0	0	0	0	0	0
Glass & Glazing	Lockheed Window Corp	0	0	0	0	0	0	0
Doors, Frames & Hardware		0	0	0	0	0	0	0
Overhead Doors		0	0	0	0	0	0	0
Aluminum Entrances & Storefronts		0	0	0	0	0	0	0
Windows	Lockheed Window Corp	0	0	0	0	0	0	0
Tile	Allegheny Contract	0	0	0	0	0	0	0
Acoustical Tile	H. Carr & Sons	0	0	0	0	0	0	0
Resilient Flooring	Allegheny Contract	0	0	0	0	0	0	0
Painting	Homer Contracting	0	0	0	0	0	0	0
GWB & Framing	Century Drywall	0	0	0	0	0	0	0
Wood Flooring		0	0	0	0	0	0	0
Wall Coverings		0	0	0	0	0	0	0
Lab Casework		0	0	0	0	0	0	0
Specialties		0	0	0	0	0	0	0
Auditorium Seating		0	0	0	0	0	0	0
Equipment		0	0	0	0	0	0	0
Bleachers		0	0	0	0	0	0	0
Gym Equipment		0	0	0	0	0	0	0
Furnishings		0	0	0	0	0	0	0
Furnishings		0	0	0	0	0	0	0
Elevators	Kone	0	0	0	0	0	0	0
Fire Protection	Hampshire Fire Protection	0	0	0	0	0	0	0

Site Rep. - Bob Smith

WEEKLY REPORT #22 - Week Ending 4/01/23

Plumbing	Araujo Brothers Plumbing	3	3	3	3	2	0	14
HVAC	General Mechanical	0	0	0	0	0	0	0
Electrical - BP1&2	Jupiter Electric	0	0	0	0	0	0	0
Electrical - BP3	Griffin Electric	0	0	0	0	0	0	0
Telecom		0	0	0	0	0	0	0
Security		0	0	0	0	0	0	0
Earthwork	Cheseapeake Geothermal	3	3	3	0	0	0	9
Landscaping		0	0	0	0	0	0	0
Playground Equipment		0	0	0	0	0	0	0
Temp. Fencing	Riggs	0	0	0	0	0	0	0
Geothermal Eng.	McPhail Associates	2	1	1	0	0	0	4
Total Weekly Manpower		56	55	64	58	44	0	277

Weekly Progress

Installation of underground sanitary and storm piping began in area "A". Continuation of storm drainage work on future entry/exit driveway installing piping, drain manholes #224 and #250. Excavation in area "D" continued with the perimeter foundation walls and interior footings. Set forms, tied rebar for footings and South and West walls in area "D" auditorium and spartan place. Installed blindside waterproofing beneath orchestra pit and LULA pit in area "D". Placed concrete for East and partial South perimeter foundation walls in area "D". Steel erection continued in area "B" East and West sides. Area "B" and "C" structural steel detailing continued with welding and bolting connections. Metal decking installation continued in area "C" and started in area "B". Installation of Nelson studs onto metal decking on second floor area "C" has begun. The rock crusher on the North field has continued to crush the excess blast rock into 6" minus ordinary fill. Geothermal flushing and filtering any dirt particles from system and pressure testing entire system has been completed.

Project Schedule Key Dates:	Activity ID	Baseline Start Finish Dates	Actual Start Finish Dates	Comments
Geothermal Wells Start	A7090	8/9/2022	10/10/2022	
Geothermal Wells Complete	A8030	4/18/2023	3/29/2023	Geothermal work is complete, filtered & tested.
Concrete foundations Start	A8020	9/28/2022	10/31/2022	
Concrete Foundations Complete	A9120	2/10/2023		Completion date pushed out to April in area "D"
Structural Steel Start	A8160	3/28/2023	3/13/2023	
Structural Steel Complete	A10610	8/24/2023		

Photos

All images need the consent of Consigli Construction prior to being released to the public.



EXCAVATING FOR UNDERGROUND PLUMBING




INSTALLATION OF SANITARY & STORM DRAIN PIPE



INSTALLATION OF DRAIN MANHOLE #250




CRUSHING BLAST ROCK ON THE NORTH FIELD

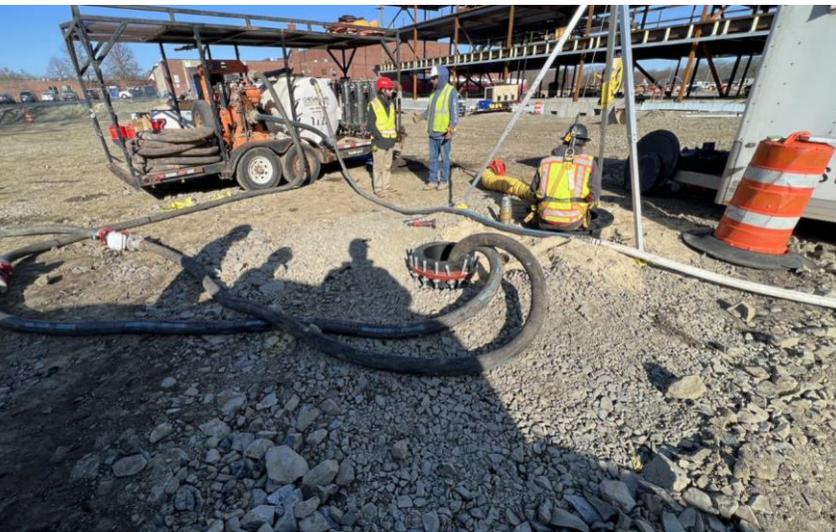

GEOHERMAL FINAL FLUSHING, FILTERING & TESTING



ORCHESTRA PIT FOOTING WATERPROOFED

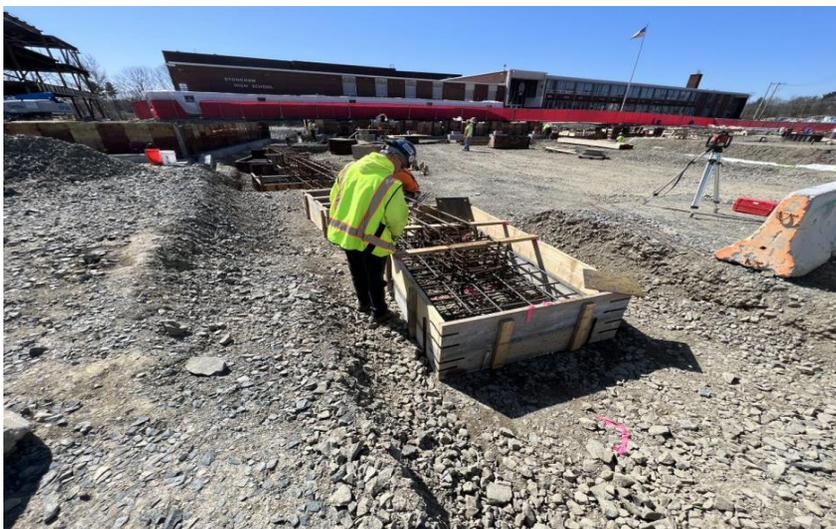

3rd PARTY INSPECTING REBAR



PLACING CONCRETE FOR AREA "D" WALLS



AUDITORIUM AND SPARTAN PLACE - AREA "D" PROGRESS FROM SHS ROOF



ACADEMIC WING - AREA "B" PROGRESS FROM SHS ROOF



ACADEMIC WING - AREA "C" PROGRESS FROM SHS ROOF



300 TON CRANE SET UP IN FUTURE GYMNASIUM TO LIFT 100 FOOT LONG AREA "B" ROOF TRUSSES
