


ID	Task Name	Duration	Start	Finish	Preced	Oct	Nov	Dec	2024	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	
1	Notice To proceed	0 days	Mon 11/20/23	Mon 11/20/23																		
2	Design Phase	90 days	Mon 11/20/23	Fri 3/22/24																		
3	SD Phase	20 days	Mon 11/20/23	Fri 12/15/23	1																	
4	DD Phase	40 days	Mon 12/18/23	Fri 2/9/24	3																	
5	CD Phase	30 days	Mon 2/12/24	Fri 3/22/24	4																	
6	Bid Phase	35 days	Mon 3/25/24	Fri 5/10/24																		
7	Publish in Central Regsiter/ Start Bid Period	5 days	Mon 3/25/24	Fri 3/29/24	5																	
8	Pre-Bid Walkthrough	6 days	Mon 4/1/24	Mon 4/8/24	7																	
9	Filed Sub Bids Due	15 days	Mon 4/1/24	Fri 4/19/24	7																	
10	General Bids Due	5 days	Mon 4/22/24	Fri 4/26/24	9																	
11	Tally/ Award	10 days	Mon 4/29/24	Fri 5/10/24	10																	
12	Construction Phase	128 days	Fri 5/10/24	Wed 11/6/24																		
13	Notice To Proceed	0 days	Fri 5/10/24	Fri 5/10/24	11																	
14	Sustantial Completion	108 days	Mon 5/13/24	Wed 10/9/24	13																	
15	Final Completion	20 days	Thu 10/10/24	Wed 11/6/24	14																	

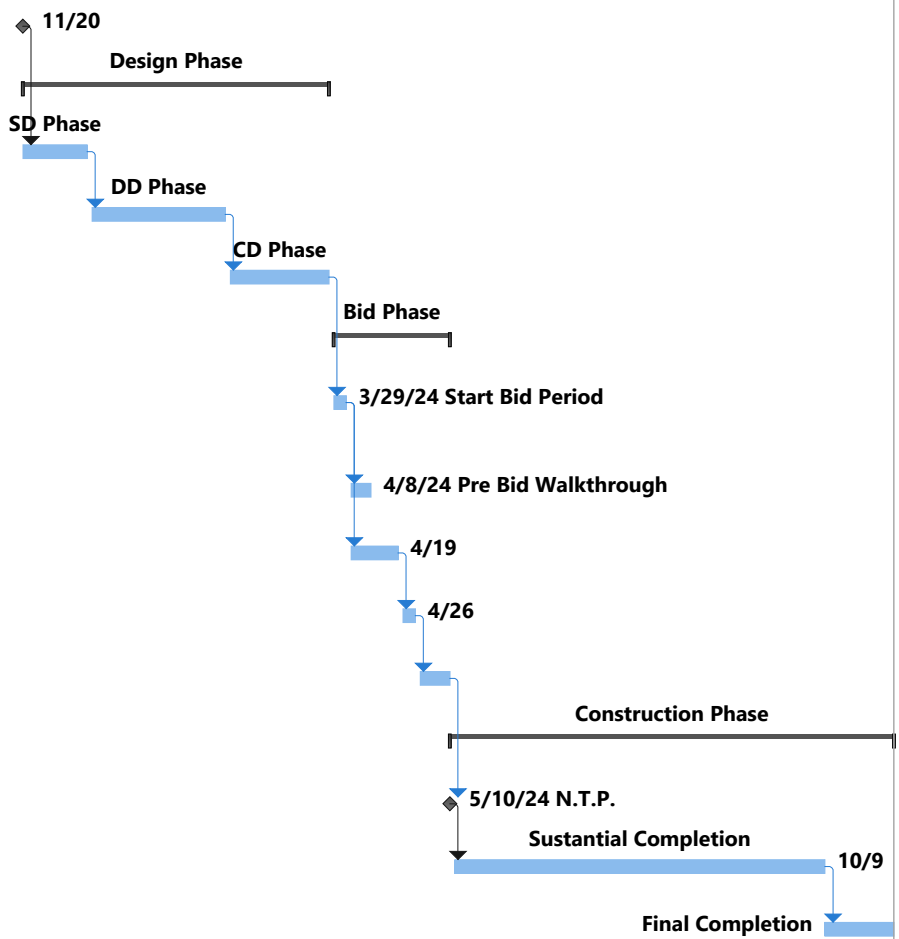

Project: 490 William Street Renovation Project Schedule-010-25
Date: Fri 11/3/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
