September 8, 2020
Updated March 24, 2022

Stoneham High School
Project Schedule

PROJECT MANAGEMENT SMMA

ID	Task Name	Duration	Start	Finish
1	**MSBA PREREQUISITES**	**158 days**	**3/22/2019**	**10/30/2019**
2	Statement of Interest (SOI) Submission	0 days	3/22/2019	3/22/2019
3	MSBA Invite into Eligibility	0 days	10/30/2019	10/30/2019
4	**RETAIN OPM**	**33 days**	**1/22/2020**	**3/9/2020**
5	Submit OPM Proposals	0 days	1/22/2020	1/22/2020
6	OPM Interview	2 days	2/6/2020	2/7/2020
7	Negotiate OPM Contract	2 days	2/7/2020	2/10/2020
8	Submit Documents to MSBA OPM Panel	0 days	2/12/2020	2/12/2020
9	**MSBA OPM Panel Meeting**	**0 days**	**3/9/2020**	**3/9/2020**
10	**RETAIN DESIGNER**	**95 days**	**2/12/2020**	**6/23/2020**
11	Draft Designer RFS and Submit to MSBA	9 days	2/12/2020	2/24/2020
12	MSBA Approve Draft RFS	7 days	3/10/2020	3/18/2020
13	Submit to Central Register	0 days	3/19/2020	3/19/2020
14	Notice in Central Register	0 days	3/25/2020	3/25/2020
15	Briefing Session	0 days	4/8/2020	4/8/2020
16	Submit Designer Proposals	0 days	4/22/2020	4/22/2020
17	**MSBA DSP Proposal Review Meeting**	**0 days**	**6/2/2020**	**6/2/2020**
18	**MSBA DSP Interview Meeting**	**0 days**	**6/16/2020**	**6/16/2020**
19	Negotiate Designer Contract	5 days	6/17/2020	6/23/2020
20	**FEASIBILITY STUDY (FS)**	**156 days**	**7/8/2020**	**2/11/2021**
21	**Develop Preliminary Design Program (PDP)**	**64 days**	**7/8/2020**	**10/6/2020**
22	**Visioning Workshops**	**9 days**	**7/20/2020**	**7/31/2020**
23	Visioning Workshop 1	0 days	7/20/2020	7/20/2020
24	Visioning Workshop 2	0 days	7/21/2020	7/21/2020
25	Visioning Workshop 3	0 days	7/23/2020	7/23/2020
26	Visioning Workshop 4	0 days	7/24/2020	7/24/2020
27	Visioning Workshop 5	0 days	7/27/2020	7/27/2020
28	Visioning Workshop 6	0 days	7/28/2020	7/28/2020
29	Visioning Workshop 7	0 days	7/30/2020	7/30/2020
30	Visioning Workshop 8	0 days	7/31/2020	7/31/2020
31	Existing Conditions Analysis	28 days	7/8/2020	8/14/2020
32	Educational Program Development	15 days	7/27/2020	8/14/2020
33	Space Template Development	15 days	7/27/2020	8/14/2020
34	Sustainable Design	31 days	7/20/2020	8/31/2020
35	Design Alternatives	41 days	8/3/2020	9/28/2020
36	Cost Models	31 days	8/17/2020	9/28/2020
37	Community Forum No. 1	0 days	8/11/2020	8/11/2020
38	Submit Project Notification Form to MHC	0 days	8/27/2020	8/27/2020
39	MHC Approval Letter	0 days	9/15/2020	9/15/2020
40	Community Forum No. 2	0 days	9/23/2020	9/23/2020
41	**Submit PDP to MSBA Staff**	**0 days**	**10/6/2020**	**10/6/2020**
42	**Develop Preferred Schematic Report (PSR)**	**91 days**	**10/7/2020**	**2/11/2021**
43	Refine Site Plans	34 days	10/7/2020	11/23/2020
44	Refine Construction Phasing Plans	34 days	10/7/2020	11/23/2020
45	Develop Floor Plans	34 days	10/7/2020	11/23/2020
46	Develop Structural Systems Narrative	9 days	10/14/2020	10/26/2020
47	Develop MEP Systems Narrative	19 days	10/14/2020	11/9/2020
48	Develop ZNE Systems	19 days	10/14/2020	11/9/2020
49	Tri-Board Meeting No. 1	0 days	10/15/2020	10/15/2020
50	PTO Meetings	23 days	10/15/2020	11/15/2020
51	Community Survey No. 1	6 days	11/5/2020	11/12/2020
52	Community Forum No. 3	0 days	11/7/2020	11/7/2020
53	Develop Cost Models	11 days	11/23/2020	12/7/2020
54	Update Site Plans and Floor Plans	11 days	11/23/2020	12/7/2020
55	Community Survey No. 2	6 days	12/8/2020	12/15/2020
56	Community Forum No. 4	0 days	12/9/2020	12/9/2020
57	Tri-Board Meeting	0 days	12/15/2020	12/15/2020
58	Select Preferred Alternative	0 days	12/16/2020	12/16/2020
59	Assemble PSR Documents	6 days	12/16/2020	12/23/2020
60	**Submit PSR to MSBA FAS**	**0 days**	**12/23/2020**	**12/23/2020**
61	**MSBA FAS Meeting**	**0 days**	**1/13/2021**	**1/13/2021**
62	**MSBA Board Meeting**	**0 days**	**2/11/2021**	**2/11/2021**

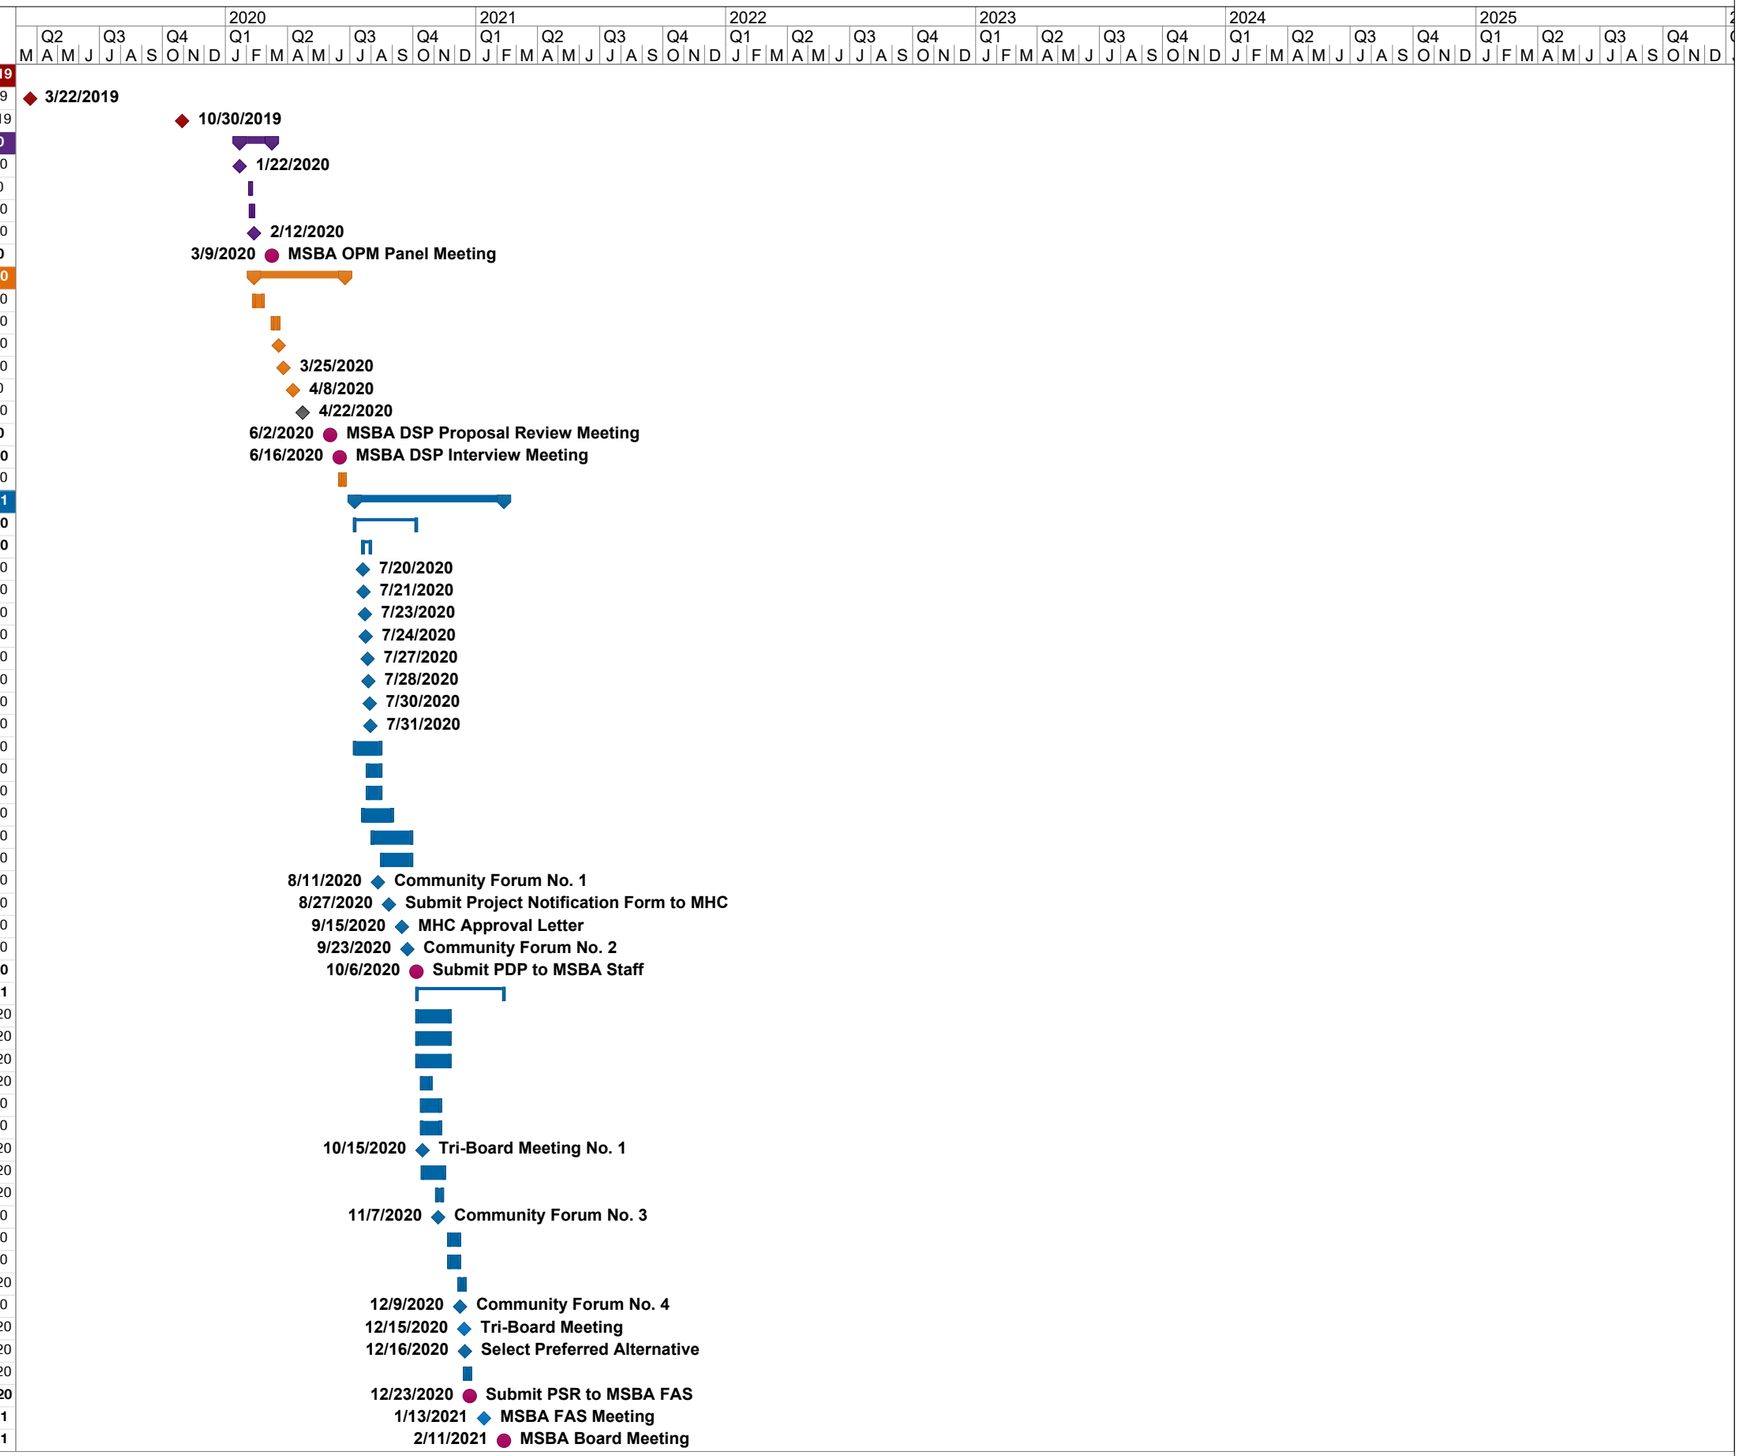

September 8, 2020
Updated March 24, 2022

Stoneham High School
Project Schedule

PROJECT MANAGEMENT SMMA

ID	Task Name	Duration	Start	Finish
63	**CONSTRUCTION MANAGER (CM)**	**99 days**	**10/13/2020**	**2/26/2021**
64	Develop and Submit IG Application	5 days	10/13/2020	10/19/2020
65	IG Application and Approval	36 days	10/19/2020	12/7/2020
66	Issue RFQ	0 days	11/11/2020	11/11/2020
67	Qualification Packages Due	0 days	12/2/2020	12/2/2020
68	Short List CM Firms	0 days	1/4/2021	1/4/2021
69	Issue RFP	0 days	1/11/2021	1/11/2021
70	Proposal Packages Due	0 days	1/25/2021	1/25/2021
71	Interview	0 days	2/10/2021	2/10/2021
72	Recommend CM to SSBC	0 days	2/22/2021	2/22/2021
73	Negotiate CM Contract	5 days	2/22/2021	2/26/2021
74	**SCHEMATIC DESIGN (SD)**	**198 days**	**1/4/2021**	**10/6/2021**
75	Develop Site Plans	31 days	1/4/2021	2/15/2021
76	Develop Floor Plans	31 days	1/4/2021	2/15/2021
77	Develop Construction Phasing Plans	31 days	1/4/2021	2/15/2021
78	Develop Building Exterior Design	36 days	2/1/2021	3/22/2021
79	Geotechnical Exploration and Findings	16 days	2/1/2021	2/22/2021
80	Develop MEP Systems Narrative	16 days	2/15/2021	3/8/2021
81	Develop Sustainable Design Features	16 days	2/15/2021	3/8/2021
82	Develop Security and Access Control	16 days	2/15/2021	3/8/2021
83	Develop Structural Systems Narrative	21 days	2/15/2021	3/15/2021
84	Refine Site Plans and Floor Plans	41 days	2/15/2021	4/12/2021
85	Refine Exterior Elevations	41 days	2/15/2021	4/12/2021
86	Refine Structural Systems	41 days	2/15/2021	4/12/2021
87	Refine MEP Systems	41 days	2/15/2021	4/12/2021
88	Refine Sustainable Design Features	41 days	2/15/2021	4/12/2021
89	Community Forum No. 5	0 days	2/24/2021	2/24/2021
90	Community Forum No. 6	0 days	3/24/2021	3/24/2021
91	Tri-Board Meeting No. 3	0 days	3/30/2021	3/30/2021
92	Issue Site Pricing Set to Estimator and CM	0 days	5/3/2021	5/3/2021
93	Town Meeting	0 days	5/3/2021	5/3/2021
94	Develop Schematic Design Estimate	26 days	5/3/2021	6/7/2021
95	Issue Engineering Pricing Set to Estimator and CM	0 days	5/17/2021	5/17/2021
96	Issue Architectural Pricing Set to Estimator and CM	0 days	5/24/2021	5/24/2021
97	Community Forum No. 7	0 days	5/26/2021	5/26/2021
98	Develop Room Data Sheets	20 days	6/1/2021	6/28/2021
99	Cost Estimate Due	0 days	6/7/2021	6/7/2021
100	Estimate Reconciliation Meeting	0 days	6/10/2021	6/10/2021
101	Reconcile Estimates	4 days	6/7/2021	6/10/2021
102	Value Engineering	6 days	6/7/2021	6/14/2021
103	Tri-Board Meeting No. 4	0 days	6/8/2021	6/8/2021
104	Reconciled Estimates Due	0 days	6/11/2021	6/11/2021
105	Present SD Cost Estimate and Progress VE to SSBC	0 days	6/14/2021	6/14/2021
106	Final VE Pricing	0 days	6/18/2021	6/18/2021
107	Present Value Engineering to SSBC	0 days	6/21/2021	6/21/2021
108	SSBC Vote to Approve Final Budget	0 days	6/21/2021	6/21/2021
109	**Submit Final Budget to MSBA**	**0 days**	**6/23/2021**	**6/23/2021**
110	**Submit Schematic Design to MSBA**	**0 days**	**7/7/2021**	**7/7/2021**
111	MSBA Review SD Comments	16 days	7/7/2021	7/28/2021
112	Respond to MSBA SD Comments	11 days	7/28/2021	8/11/2021
113	**MSBA Board Meeting**	**0 days**	**8/25/2021**	**8/25/2021**
114	PS&B Agreement Execution	21 days	8/25/2021	9/22/2021
115	DESE Review	21 days	8/25/2021	9/22/2021
116	MSBA Review of DESE Submittal	11 days	9/22/2021	10/6/2021
117	**LOCAL APPROPRIATION**	**122 days**	**6/24/2021**	**12/10/2021**
118	Draft Town Meeting and Ballot Articles	10 days	6/24/2021	7/7/2021
119	Town Council / Bond Council Approve Articles	16 days	7/7/2021	7/28/2021
120	MSBA Approve Articles	16 days	7/28/2021	8/18/2021
121	Select Board Mtg Schedule Ballot Vote	0 days	8/31/2021	8/31/2021
122	**Annual Fall Town Meeting**	**0 days**	**10/4/2021**	**10/4/2021**
123	**Debt Exclusion Ballot Vote**	**0 days**	**11/2/2021**	**11/2/2021**
124	Certification of Votes Sent to MSBA	6 days	11/3/2021	11/10/2021
125	Project Funding Agreement Execution	23 days	11/10/2021	12/10/2021

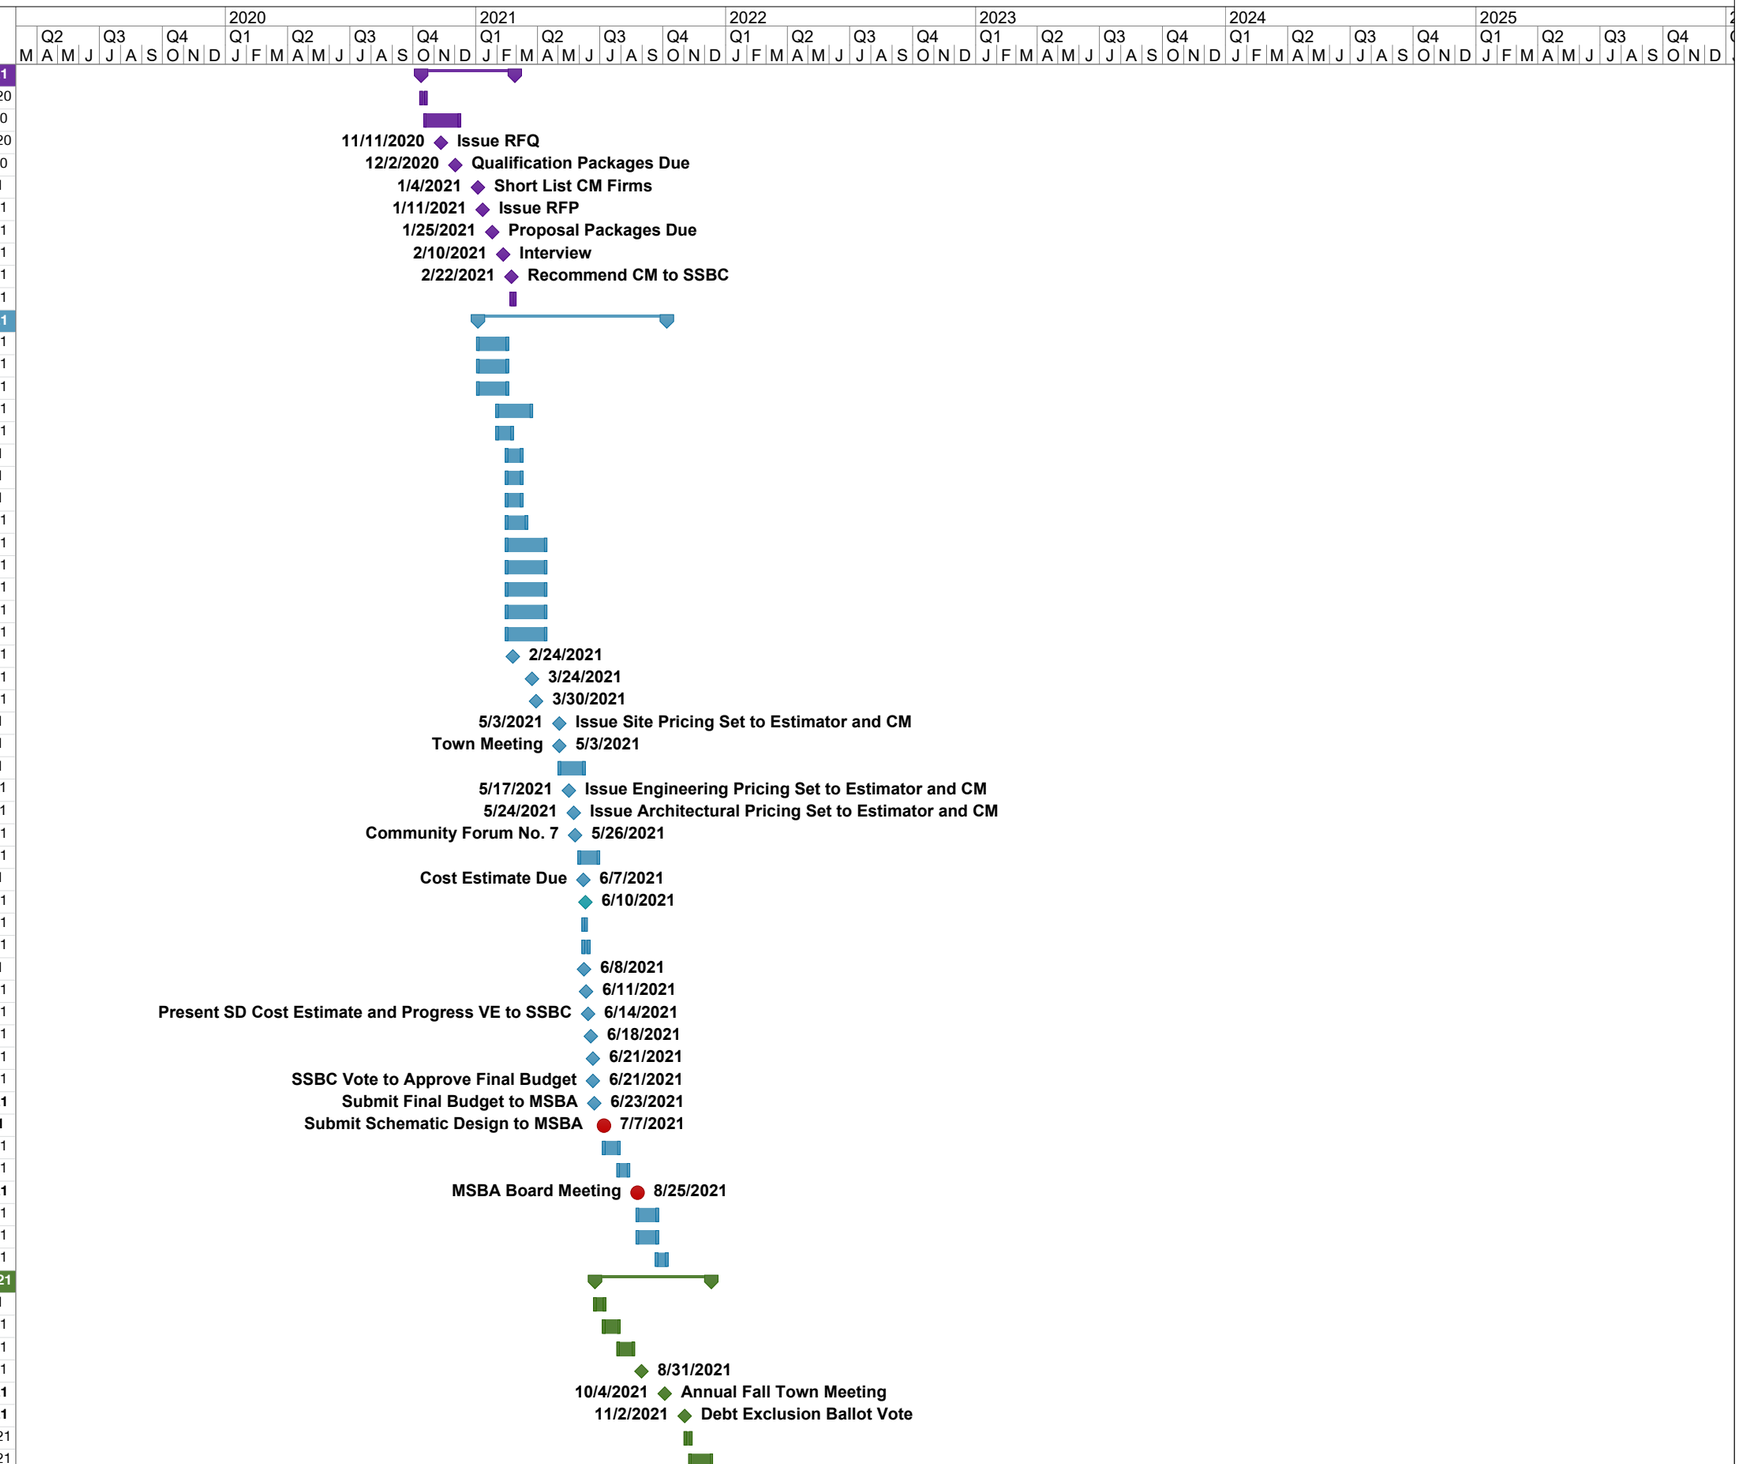

September 8, 2020
Updated March 24, 2022

Stoneham High School
Project Schedule

PROJECT MANAGEMENT SMMA

ID	Task Name	Duration	Start	Finish
126	**PHOTOVOLTAIC VENDOR**	**212 days**	**6/15/2021**	**4/6/2022**
127	Retain PV RFP Consultant	114 days	6/15/2021	11/19/2021
128	Draft RFP	29 days	11/19/2021	12/29/2021
129	Issue RFP	0 days	12/29/2021	12/29/2021
130	PV Vendor Develop Proposal	38 days	12/29/2021	2/18/2022
131	Review Photovoltaic Vendor Proposals and Interview	12 days	2/18/2022	3/7/2022
132	Short List Prospective Photovoltaic Vendors	0 days	3/7/2022	3/7/2022
133	Interview Prospective Vendors	0 days	3/15/2022	3/15/2022
134	Negotiation and Award	16 days	3/16/2022	4/6/2022
135	**DESIGN DEVELOPMENT**	**125 days**	**11/8/2021**	**4/29/2022**
136	SBC Approve DD-CA Agreements	0 days	11/8/2021	11/8/2021
137	LEED-S Registration	16 days	11/8/2021	11/29/2021
138	Prepare DD Pricing Set	81 days	11/8/2021	2/28/2022
139	Geothermal Conductivity Test Prep	0 days	12/6/2021	12/6/2021
140	Survey Off-Site	12 days	12/6/2021	12/21/2021
141	Background Noise Study	6 days	12/10/2021	12/17/2021
142	Geothermal Conductivity Test	4 days	12/13/2021	12/16/2021
143	DD Programming Meetings	28 days	12/15/2021	1/21/2022
144	Geotechnical Test Pits	2 days	12/20/2021	12/21/2021
145	Survey On-Site	24 days	12/21/2021	1/21/2022
146	Geotechnical Borings	5 days	12/22/2021	12/28/2021
147	GeoEnvironmental Probes	2 days	12/23/2021	12/24/2021
148	Hazardous Materials Investigation	4 days	12/27/2021	12/30/2021
149	Hazardous Materials Investigation	4 days	2/22/2022	2/25/2022
150	Issue Complete DD Pricing Set	0 days	2/28/2022	2/28/2022
151	OPM and Cx Review	10 days	2/28/2022	3/11/2022
152	Estimates Due from PM&C and Consigli	0 days	3/18/2022	3/18/2022
153	Estimate Reconciliation Meeting	0 days	3/22/2022	3/22/2022
154	Revised Reconciled Estimates Due	0 days	3/24/2022	3/24/2022
155	Present CM Cost Estimate and Value Engineering List to SSBC	0 days	3/28/2022	3/28/2022
156	Present Final Value Engineering to SSBC	0 days	4/4/2022	4/4/2022
157	SSBC Vote to Approve Design Development Submission	0 days	4/4/2022	4/4/2022
158	**Design Development Submission to MSBA**	**0 days**	**4/8/2022**	**4/8/2022**
159	MSBA Comments	15 days	4/11/2022	4/29/2022
160	**SITE PERMITTING**	**167 days**	**11/8/2021**	**6/28/2022**
161	**Stoneham Conservation Commission - ANRAD (Not Required - Delineation Reviewed with NOI)**	**42 days**	**11/8/2021**	**1/4/2022**
168	**Stoneham Conservation Commission - NOI**	**167 days**	**11/8/2021**	**6/28/2022**
169	Prepare Application Documents	123 days	11/8/2021	4/27/2022
170	File Application	0 days	4/27/2022	4/27/2022
171	Hearing No. 1	0 days	5/2/2022	5/2/2022
172	Hearing No. 2	0 days	5/23/2022	5/23/2022
173	Conservation Commission Issue Order of Conditions	15 days	5/24/2022	6/13/2022
174	Record at Registry of Deeds	1 day	6/14/2022	6/14/2022
175	Appeal Period	10 days	6/15/2022	6/28/2022
176	**Stormwater Board Approval**	**23 days**	**4/27/2022**	**5/30/2022**
177	Submit Stormwater Board Approval Application	0 days	4/27/2022	4/27/2022
178	Hearing No. 1	0 days	5/9/2022	5/9/2022
179	Hearing No. 2	0 days	5/30/2022	5/30/2022
180	Stormwater Award Approval	0 days	5/30/2022	5/30/2022
181	**Zoning Board of Appeals**	**42 days**	**4/27/2022**	**6/23/2022**
182	Submit Variance Request	0 days	4/27/2022	4/27/2022
183	Hearing No. 1	0 days	5/12/2022	5/12/2022
184	Hearing No. 2	0 days	5/26/2022	5/26/2022
185	ZBA Issues Decision	0 days	6/3/2022	6/3/2022
186	Record at Registry of Deeds	0 days	6/3/2022	6/3/2022
187	Appeal Period	15 days	6/3/2022	6/23/2022
188	**Stoneham Select Board - Site Plan Approval (Not Required)**	**159 days**	**11/8/2021**	**6/16/2022**
197	**BUILDING PERMITTING**	**228 days**	**1/19/2022**	**12/2/2022**
198	**State Building Code Variance**	**58 days**	**1/19/2022**	**4/11/2022**
199	Submit Variance Denial Letter Request	0 days	1/19/2022	1/19/2022
200	Building Commissioner Issue Denial Letter	16 days	1/20/2022	2/10/2022
201	Submit Variance Request	0 days	2/24/2022	2/24/2022

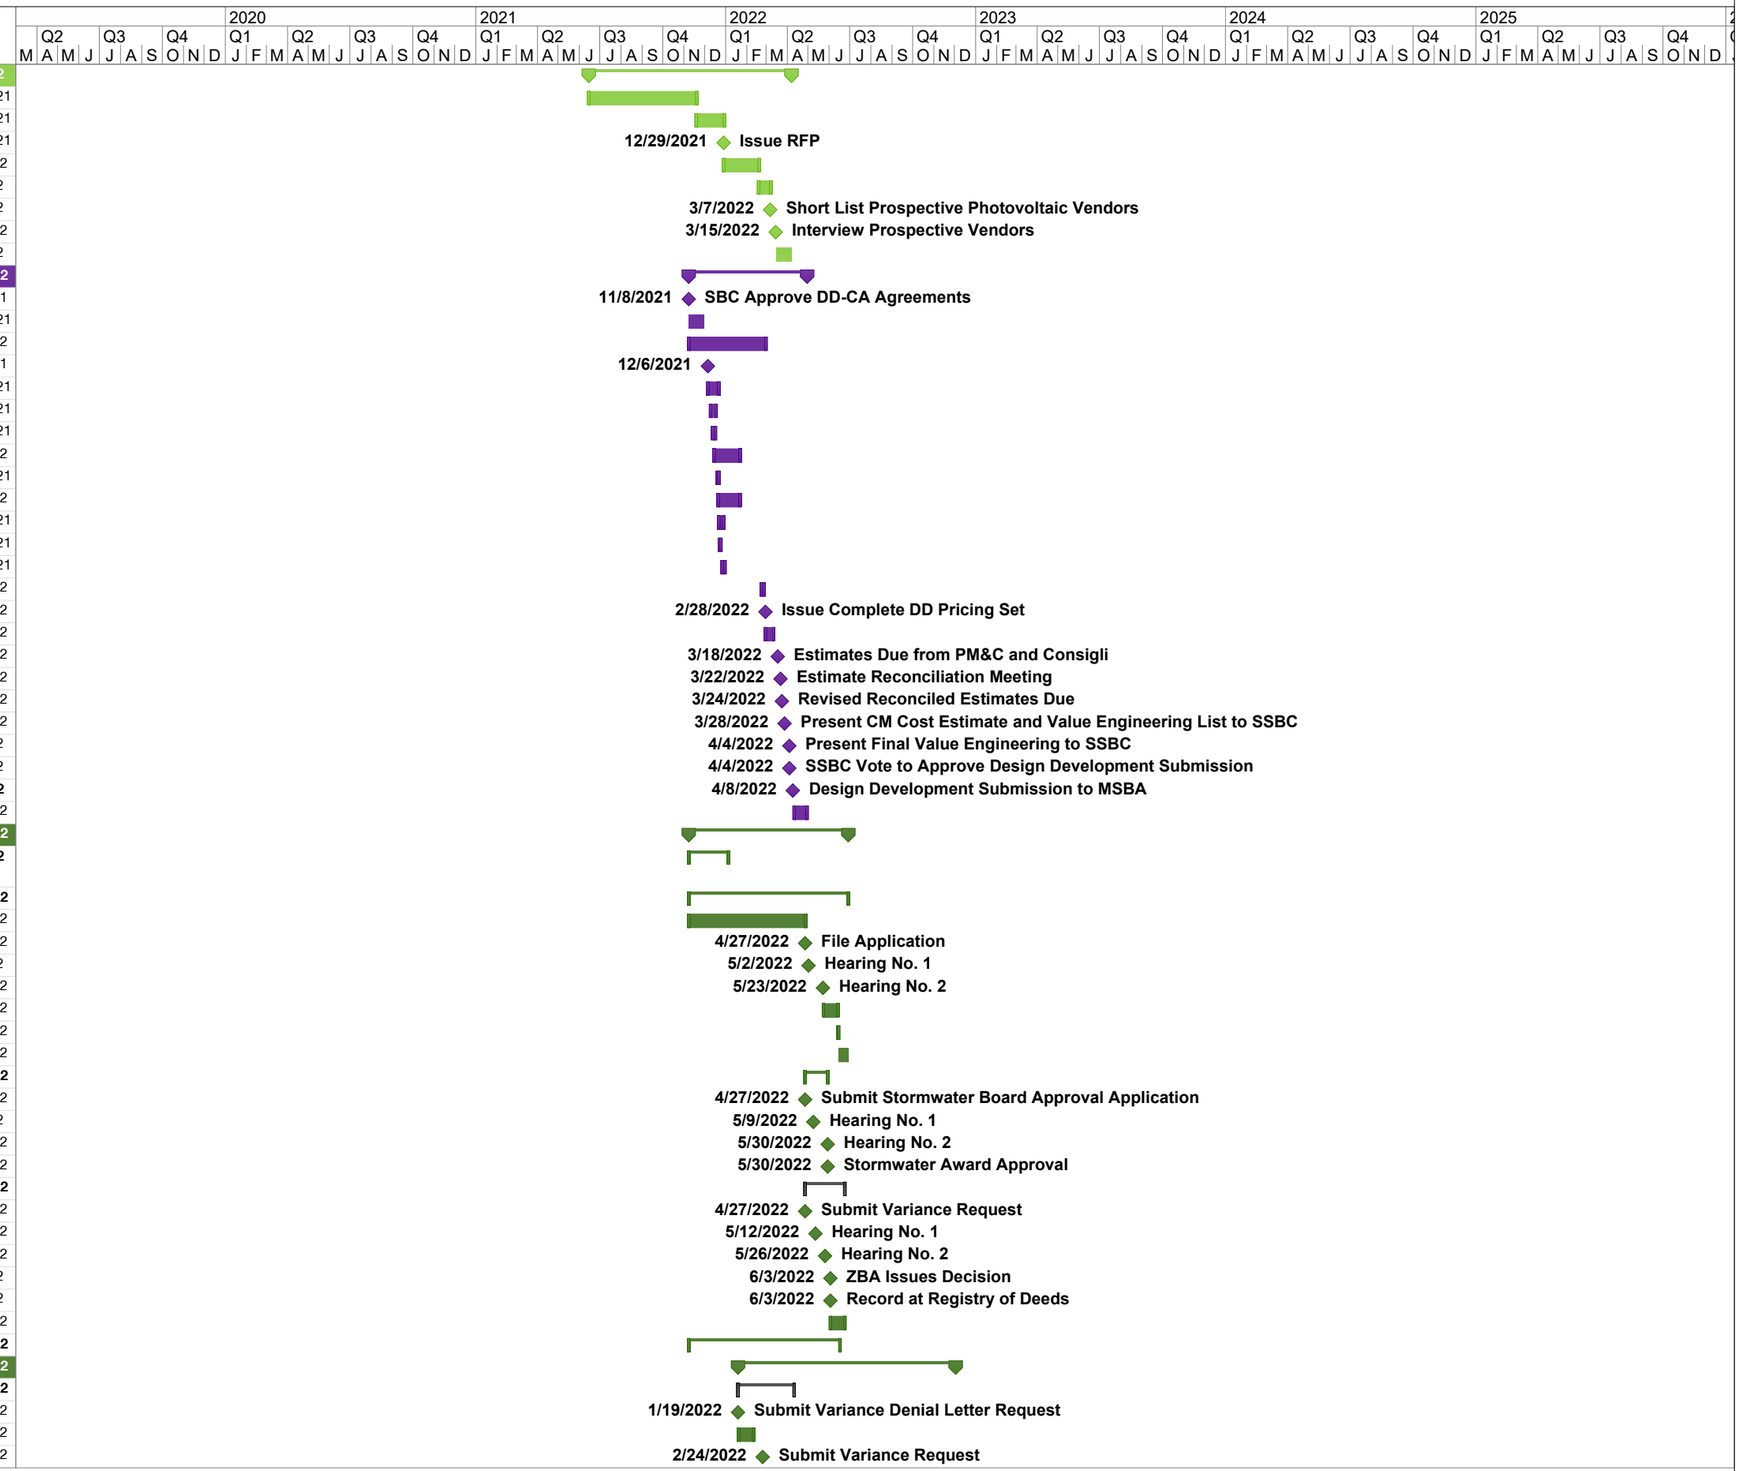

September 8, 2020
Updated March 24, 2022

Stoneham High School
Project Schedule

PROJECT MANAGEMENT SMMA

ID	Task Name	Duration	Start	Finish
202	Hearing No. 1	0 days	3/22/2022	3/22/2022
203	Issue Variance Approval	0 days	4/11/2022	4/11/2022
204	**MAAB Variance**	**12 days**	**3/24/2022**	**4/11/2022**
205	Submit Variance Request	0 days	3/24/2022	3/24/2022
206	Hearing No. 1	0 days	4/11/2022	4/11/2022
207	Issue Variance Approval	0 days	4/11/2022	4/11/2022
208	**Site Preparation Package Permit**	**30 days**	**5/18/2022**	**6/28/2022**
209	**Foundation Permit**	**23 days**	**6/20/2022**	**7/20/2022**
210	**Structure Permit**	**23 days**	**6/29/2022**	**7/29/2022**
211	**Building Permit**	**21 days**	**11/4/2022**	**12/2/2022**
212	**CONSTRUCTION DOCUMENTS**	**176 days**	**3/18/2022**	**11/18/2022**
213	**Early Site Enabling, and Preparation Package No. 1**	**37 days**	**3/18/2022**	**5/9/2022**
214	Incorporate MSBA DD Comments	11 days	4/29/2022	5/13/2022
215	Issue Complete 60% Construction Documents Pricing Set	0 days	5/11/2022	5/11/2022
216	OPM and Cx Review	10 days	5/11/2022	5/24/2022
217	Structural Peer Review of Early Foundation & Structural Package	10 days	5/11/2022	5/24/2022
218	PM&C and Consigli Estimating	15 days	5/11/2022	5/31/2022
219	Estimates Due from PM&C and Consigli	0 days	5/31/2022	5/31/2022
220	Estimate Reconciliation Meeting	0 days	6/2/2022	6/2/2022
221	Final Reconciled Estimates Due	0 days	6/3/2022	6/3/2022
222	Present CM Cost Estimate and Value Engineering List to SSBC	0 days	6/13/2022	6/13/2022
223	Present Value Engineering to SSBC	0 days	6/21/2022	6/21/2022
224	SSBC Vote to Approve 60% Construction Documents Submission	0 days	6/21/2022	6/21/2022
225	**Early Foundation and Structural Package No. 2**	**56 days**	**4/8/2022**	**6/24/2022**
226	**60% Construction Documents Submission to MSBA**	**0 days**	**6/24/2022**	**6/24/2022**
227	MSBA Review of 60% CD Submission	15 days	6/27/2022	7/15/2022
228	Incorporate MSBA 60% CD Comments	7 days	7/15/2022	7/25/2022
229	Develop 90% Contract Documents to Estimator	42 days	6/24/2022	8/22/2022
230	OPM and Cx Review	11 days	8/22/2022	9/5/2022
231	90% Construction Documents Cost Estimate	11 days	8/22/2022	9/5/2022
232	Value Engineering	6 days	9/5/2022	9/12/2022
233	**90% Construction Documents Submission to MSBA**	**0 days**	**9/12/2022**	**9/12/2022**
234	MSBA Review of 90% CD Submission	16 days	9/12/2022	10/3/2022
235	Incorporate MSBA 90% CD Comments	11 days	10/3/2022	10/17/2022
236	**Construction Documents Complete Package No. 3**	**0 days**	**11/4/2022**	**11/4/2022**
237	LEED-S Design Submission	11 days	11/4/2022	11/18/2022
238	**PROCUREMENT**	**235 days**	**2/15/2022**	**1/9/2023**
239	**Prequalification - Package No. 1 (if required)**	**50 days**	**2/15/2022**	**4/25/2022**
240	Draft RFQ	28 days	2/15/2022	3/24/2022
241	Submit to Advertisement to Central Register and Local Newspaper	0 days	3/24/2022	3/24/2022
242	Notice in Central Register	0 days	3/30/2022	3/30/2022
243	Submit SOQs	0 days	4/15/2022	4/15/2022
244	Review SOQs	5 days	4/18/2022	4/22/2022
245	Recommend Prequalified Subcontractors to SSBC	0 days	4/22/2022	4/22/2022
246	Issue Notification Letters to Prequalified Subcontractors	0 days	4/25/2022	4/25/2022
247	**Prequalification - Package No. 2 (if required)**	**58 days**	**3/4/2022**	**5/24/2022**
248	Draft RFQ	22 days	3/4/2022	4/4/2022
249	Submit Advertisement to Central Register and Local Newspaper	0 days	4/5/2022	4/5/2022
250	Notice in Central Register	0 days	4/13/2022	4/13/2022
251	Submit SOQs	0 days	5/2/2022	5/2/2022
252	Review SOQs	15 days	5/3/2022	5/23/2022
253	Recommend Prequalified Subcontractors to SSBC	0 days	5/23/2022	5/23/2022
254	Issue Notification Letters to Prequalified Subcontractors	0 days	5/24/2022	5/24/2022
255	**Prequalification - Package No. 3**	**63 days**	**7/15/2022**	**10/11/2022**
256	Draft RFQ	23 days	7/15/2022	8/16/2022
257	Submit Advertisement to Central Register and Local Newspaper	0 days	8/16/2022	8/16/2022
258	Notice in Central Register	0 days	8/24/2022	8/24/2022
259	Submit SOQs	0 days	9/12/2022	9/12/2022
260	Review SOQs	16 days	9/12/2022	10/3/2022
261	Recommend Prequalified Subcontractors to SBC	0 days	10/10/2022	10/10/2022
262	Issue Notification Letters to Prequalified Subcontractors	0 days	10/11/2022	10/11/2022
263	**Construction Documents Complete Package No. 3**	**55 days**	**10/25/2022**	**1/9/2023**

September 8, 2020
Updated March 24, 2022

Stoneham High School
Project Schedule

PROJECT MANAGEMENT SMMA
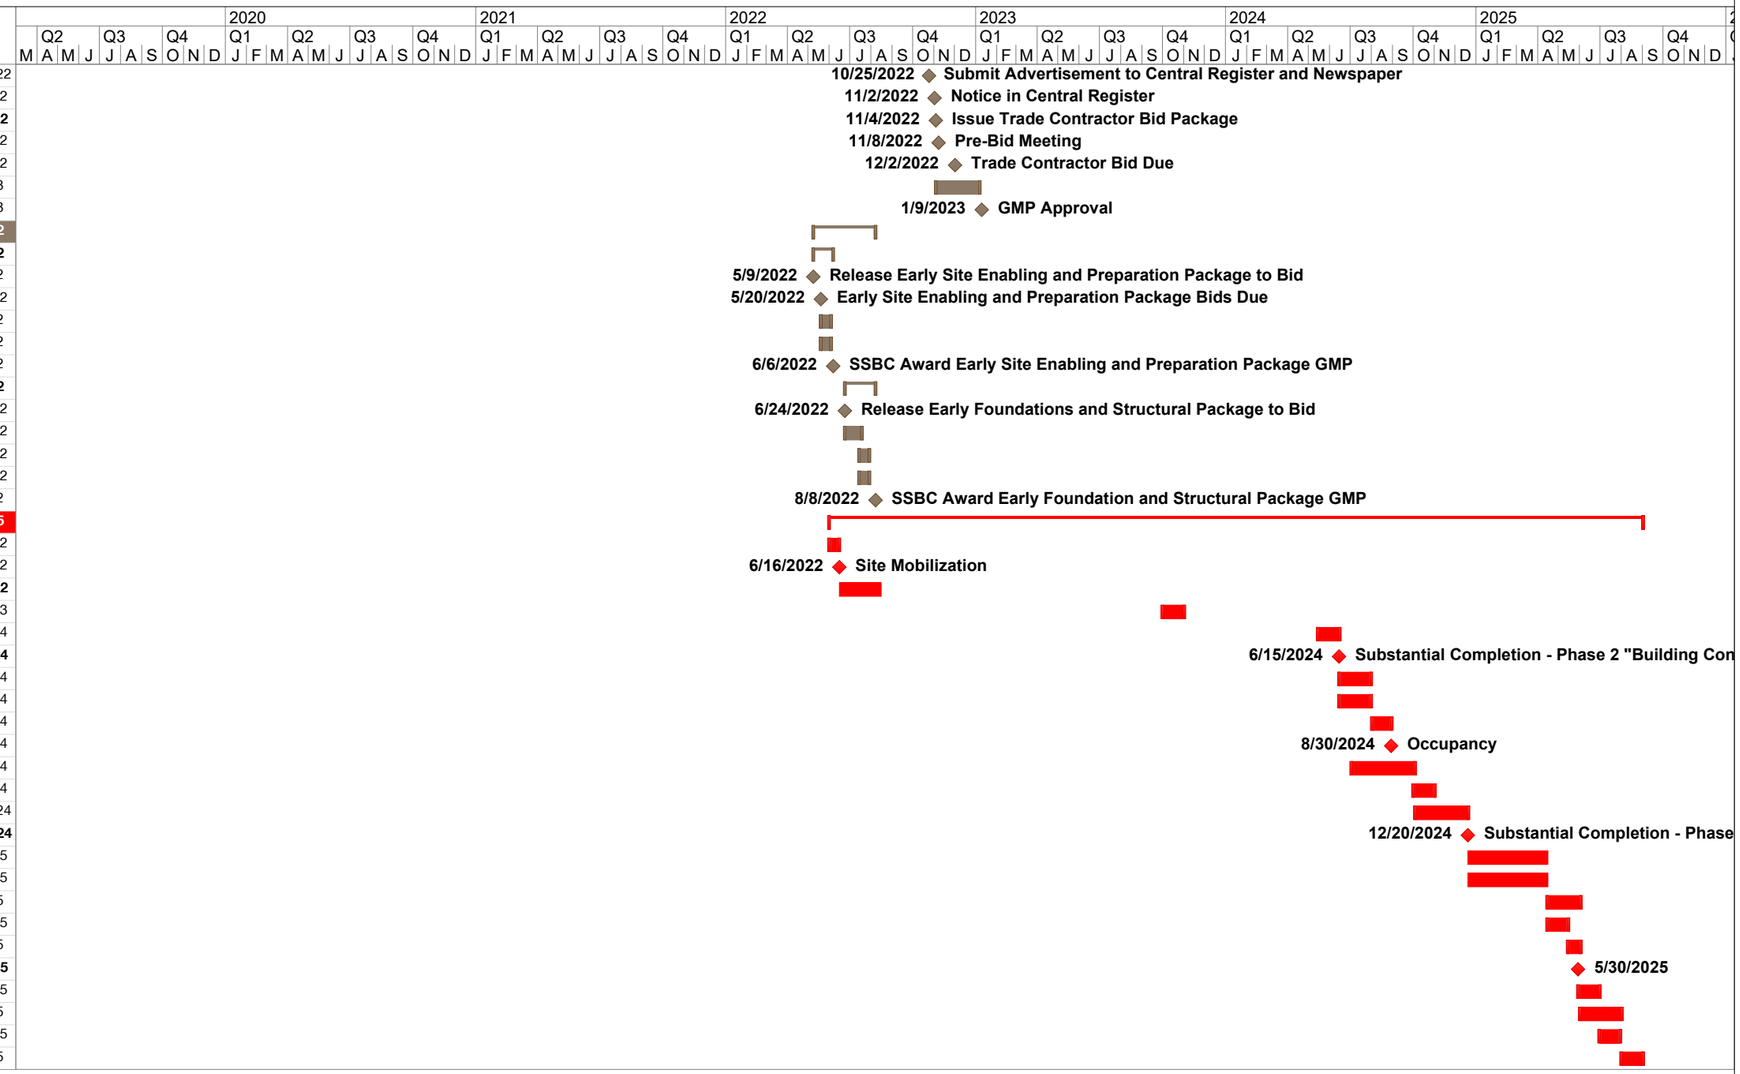
ID	Task Name	Duration	Start	Finish
264	Submit Advertisement to Central Register and Newspaper	0 days	10/25/2022	10/25/2022
265	Notice in Central Register	0 days	11/2/2022	11/2/2022
266	**Issue Trade Contractor Bid Package**	**0 days**	**11/4/2022**	**11/4/2022**
267	Pre-Bid Meeting	0 days	11/8/2022	11/8/2022
268	Trade Contractor Bid Due	0 days	12/2/2022	12/2/2022
269	CM Develop GMP	46 days	11/4/2022	1/6/2023
270	GMP Approval	0 days	1/9/2023	1/9/2023
271	**EARLY PACKAGES PROCUREMENT**	**65 days**	**5/9/2022**	**8/8/2022**
272	**Early Site Enabling Package No. 1**	**21 days**	**5/9/2022**	**6/6/2022**
273	Release Early Site Enabling and Preparation Package to Bid	0 days	5/9/2022	5/9/2022
274	Early Site Enabling and Preparation Package Bids Due	0 days	5/20/2022	5/20/2022
275	Descope Early Site Enabling and Preparation Package	11 days	5/20/2022	6/3/2022
276	Develop Early Site Enabling and Preparation Package GMP	11 days	5/20/2022	6/3/2022
277	SSBC Award Early Site Enabling and Preparation Package GMP	0 days	6/6/2022	6/6/2022
278	**Early Foundation and Structural Package No. 2**	**31 days**	**6/24/2022**	**8/8/2022**
279	Release Early Foundations and Structural Package to Bid	0 days	6/24/2022	6/24/2022
280	Early Foundation and Structural Package Bids Due	17 days	6/24/2022	7/18/2022
281	Descope Early Foundations and Structural Package	11 days	7/15/2022	7/29/2022
282	Develop Early Foundation and Structural Package GMP	11 days	7/15/2022	7/29/2022
283	SSBC Award Early Foundation and Structural Package GMP	0 days	8/8/2022	8/8/2022
284	**CONSTRUCTION**	**849 days**	**6/1/2022**	**9/1/2025**
285	CM File NPDES	11 days	6/1/2022	6/15/2022
286	Site Mobilization	0 days	6/16/2022	6/16/2022
287	**Substantial Completion - Phase 1 "Enabling Work"**	**43 days**	**6/16/2022**	**8/15/2022**
288	50% DCAMM Evaluation	24 days	10/1/2023	11/1/2023
289	Punch List Development	24 days	5/15/2024	6/15/2024
290	**Substantial Completion - Phase 2 "Building Construction"**	**0 days**	**6/15/2024**	**6/15/2024**
291	Final Completion, Closeout and Commissioning	34 days	6/15/2024	7/31/2024
292	FFE/Technology Installation	34 days	6/15/2024	7/31/2024
293	Teacher/Staff Move-In	21 days	8/2/2024	8/30/2024
294	Occupancy	0 days	8/30/2024	8/30/2024
295	Demolish Existing School	67 days	7/3/2024	10/3/2024
296	100% DCAMM Evaluation - Trades	24 days	10/1/2024	11/1/2024
297	Playfield Construction	56 days	10/4/2024	12/20/2024
298	**Substantial Completion - Phase 3 "Demolition and Site Work"**	**0 days**	**12/20/2024**	**12/20/2024**
299	Closeout	83 days	12/20/2024	4/15/2025
300	Final Completion	83 days	12/20/2024	4/15/2025
301	LEED-S Construction Submission	35 days	4/15/2025	6/2/2025
302	Cx Post Construction Inspection	23 days	4/15/2025	5/15/2025
303	Cx Final Report to MSBA	13 days	5/15/2025	6/2/2025
304	**Substantial Completion - Complete Playfields**	**0 days**	**5/30/2025**	**5/30/2025**
305	100% DCAMM Evaluation - CM	22 days	5/30/2025	6/30/2025
306	USGBC Review and Certification	45 days	6/2/2025	8/1/2025
307	CM Final Payment Request	23 days	6/30/2025	7/30/2025
308	Final Reimbursement Request	22 days	8/1/2025	9/1/2025
